



Pinelands Regional School District

Junior & Senior High School - Weekly Renovation Updates

Overall Project:

Senior High School - Masonry Restoration

- Continued installation of exterior masonry ó A-Wing elevations
- Continued installation of exterior wall preparation of steel (installation/cleaning/painting), masonry surface preparation and installation of vapor barrier system
- Continued roof coping modifications
- Continued exterior structural wall framing ó A Wing (north elev.)
- Continued installation of exterior windows & doorsó C Wing South

Senior & Junior High School - Renovations

- Continued selective interior renovations ó (Sr. High School)
- Continued bathroom renovations ó sheetrock / ceramic tile / fixtures (Sr. High School)
- Continued HVAC & electrical system renovations (Sr. High School)
- Continued new Main Entrance addition ó Exterior Brick preparation (Sr. High School)
- Continued preparation & painting for Hallways & Stairways (Sr. High School)
- Continued installation of ceiling system grid ó selective classrooms & corridors (Sr. High School)
- Continued installation interior classroom doors (Sr. High School)
- Continued 2nd shift electrical renovations (fire alarm wiring installation- summer 2019 conversion)(Jr. High School)

Senior & Junior High School – Paving & Site Improvements (Spring / Summer 2019)

Athletic Field Walkway ó Preparation

Scheduled Activities for the week of May 13 2019 thru May 17 2019

Overall Project:

Senior High School - Masonry Restoration

- Continue installation of exterior wall preparation ó steel (installation/cleaning/painting), masonry surface preparation
- Continue installation of exterior masonry \(\delta \) A Wing elevations
- Continue roof coping modifications
- Continue exterior structural wall framing ó A Wing (north elev.)
- Continue installation of interior window sills & trim (C Wing)
- Continue site concrete work (Sidewalks & Exterior door aprons) & Continue Site/Lawn restoration (A & D Wing)

Senior & Junior High School - Renovations

- Continue layout &installation of HVAC ductwork & units (Sr. High School)
- Continue layout / installation for new Main Entrance ó Exterior Brick (Sr. High School)
- Continue electrical system modifications (Sr. High School)
- Continue progressing LEHT Building Dept. Inspections
- Continue preparation & painting of interior walls (Sr. High School)
- Continue ceramic tile installation & continue plumbing fixture installation -bathroom renovations (Sr. High School)
- Continue ceiling grid & tile installation ó selective classrooms & corridors (Sr. High School)
- Continue preparation & installation of wooden corridor doors & hardware (Sr. High School)
- Continue installation of VCT floor tile (Corridors) (Sr. High School)
- Continue electrical renovations & fire alarm wiring installation- summer 2019 conversion (Jr. High School)

Senior & Junior High School – Paving & Site Improvements (Spring / Summer 2019)

Commence removal of guard-rail & installation of chain-lick fencing along Nugentown Rd.

Epic Management, Inc. Page 1 of 9





Pinelands Regional Sr. High School ó Main Entrance Gym



Pinelands Regional Sr. High School ó Gym Front Elevation

Epic Management, Inc. Page 2 of 9





Pinelands Regional Sr. High School ó Exterior Masonry Preparation (Main Entrance)



Pinelands Regional Sr. High School ó Exterior Wall Reconstruction & Masonry (Block A North)

Epic Management, Inc. Page 3 of 9



Pinelands Regional Sr. High School ó Exterior Preparation & Installation (Block A - Atrium)



Pinelands Regional Sr. High School ó Exterior Brick Installation (Block A West)

Epic Management, Inc. Page 4 of 9





Pinelands Regional Sr. High School ó Exterior Brick- Installation (Block A South)



Pinelands Regional Sr. High School ó Structural Restoration (Block A North 3rd Floor)

Epic Management, Inc. Page 5 of 9





Pinelands Regional Sr. High School ó Exterior Sidewalk Installation (Block C Rear)




Pinelands Regional Sr. High School ó Corridor Door Installation (Atrium)

Epic Management, Inc. Page 6 of 9



Pinelands Regional Sr. High School ó Ceiling System & lighting Installation (Block A North 1st Floor)

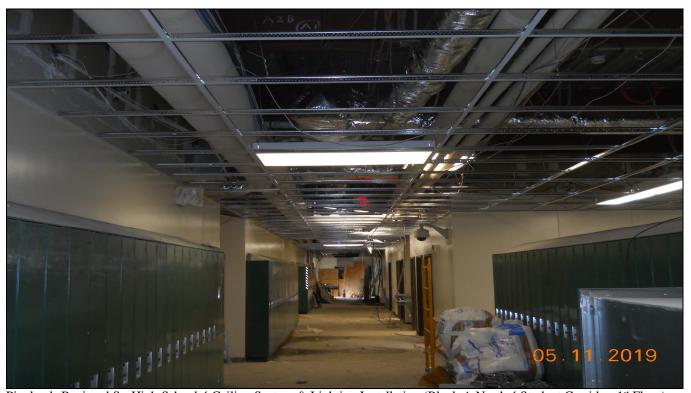

Pinelands Regional Sr. High School ó Ceiling System & Lighting Installation (Block A North ó Student Corridor 1st Floor)

Epic Management, Inc. Page 7 of 9



Pinelands Regional Sr. High School ó Student Corridor (Block A North 3rd Floor)



Pinelands Regional Sr. High School ó Student Corridor (Block A North 2nd Floor)

Epic Management, Inc. Page 8 of 9





Pinelands Regional Sr. High School ó Interior Painting (Media Center)



Pinelands Regional Sr. High School ó Interior Painting (Cafeteria)

Epic Management, Inc. Page 9 of 9
