



### **Pinelands Regional** School District

### **Junior & Senior High School Weekly Renovation Updates**

#### Overall Project:

### Senior High School - Masonry Restoration

- Continued installation of exterior masonry 6 A -Wing (west elev.) walls & C-Wing (east elev.)
- Continued installation of exterior wall preparation of steel (installation/cleaning/painting), masonry surface preparation and installation of vapor barrier system
- Continued roof coping modifications
- Continued exterior structural wall framing ó A Wing (north elev.)
- Continued site concrete work ó exterior access concrete apron/sidewalks & masonry column bases (preparation / installation)

### Senior & Junior High School - Renovations

- Continued selective interior renovations ó (Sr. High School)
- Continued bathroom renovations ó entry door frames; wall framing / sheetrock / ceramic tile (Sr. High School)
- Continued HVAC & electrical system renovations (Sr. High School)
- Continued new Main Entrance addition ó masonry walls (Sr. High School)
- Continued preparation & painting for Hallways & Stairways (Sr. High School)
- Commenced installation of ceiling system grid ó selective classrooms (Sr. High School)
- Completed 2<sup>nd</sup> floor bathroom renovations 6 Toilet Partitions / Painting & Clean-up / Township Inspections (Jr. High School)

### Scheduled Activities for the week of April 01 2019 thru April 05 2019

### **Overall Project:**

#### Senior High School - Masonry Restoration

- Continued layout / modification for new exterior window / door opening (A & C Wing)
- Continue installation of exterior wall preparation ó steel (installation/cleaning/painting), masonry surface preparation
- Continue installation of exterior masonry ó A & C Wing elevations
- Continue roof coping modifications
- Continue selective demolition ó A Wing (north wall elev.)
- Continue exterior structural wall framing ó A Wing (north elev.)
- Continue installation of roll-up overhead doors (D Wing)
- Continue site concrete work (Sidewalks & Exterior door aprons) (B & D Wing)

#### <u> Senior & Junior High School - Renovations</u>

- Continue layout &installation of HVAC ductwork & units (Sr. High School)
- Continue layout / installation for new Main Entrance (Sr. High School)
- Continue electrical system modifications (Sr. High School)
- Continue layout / installation for atrium partition walls / window & door frames (Sr. High School)
- Continue progressing LEHT Building Dept. Inspections
- Continue preparation & painting of interior walls (Sr. High School)
- Continue ceramic tile installation & commence plumbing fixture installation -bathroom renovations (Sr. High School)
- Continue ceiling grid installation ó selective classrooms (Sr. High School)
- Continue 2<sup>nd</sup> shift electrical renovations (fire alarm wiring installation- summer 2019 conversion)(Jr. High School)

#### Senior & Junior High School – Paving & Site Improvements (Summer 2019)

Construction Project ó Award Coordination

### **Epic Management, Inc.** Page 1 of 9





Pinelands Regional Sr. High School ó Exterior Wall System (Block A North)



Pinelands Regional Sr. High School ó Exterior Wall Structural Framing (Block A North)

# **Epic Management, Inc.** Page 2 of 9



Pinelands Regional Sr. High School ó Exterior Masonry Installation (Block A West)



Pinelands Regional Sr. High School ó Exterior Concrete Installation (Door Aprons & Sidewalk ó Block B West Gym)

## Epic Management, Inc. Page 3 of 9





Pinelands Regional Sr. High School ó Exterior Masonry Preparation - (Block A South)



Pinelands Regional Sr. High School ó Exterior Wall Preparation & Steel Installation (Block C South ó Media Center)

## **Epic Management, Inc.** Page 4 of 9





Pinelands Regional Sr. High School ó Exterior Wall Preparation & Steel Installation (Block C South ó Cafeteria)



Pinelands Regional Sr. High School ó Exterior Brick ó Preparation & Installation (Block C East ó Kitchen)

# **Epic Management, Inc.** Page 5 of 9





Pinelands Regional Sr. High School ó Masonry Wall Installation (Main Entrance)




Pinelands Regional Sr. High School ó Entrance Addition Block Walls (Security Vestibule & SRO Security Office)

# **Epic Management, Inc.** Page 6 of 9





Pinelands Regional Sr. High School ó Student Bathroom Ceramic Tile Installation (Block B)

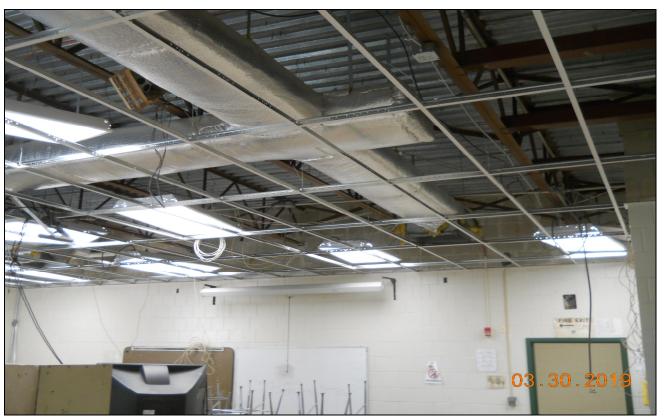

Pinelands Regional Sr. High School ó Ceiling System Grid Installation (Block D Classroom)

## **Epic Management, Inc.** Page 7 of 9

3/30/2019



Pinelands Regional Sr. High School ó Atrium Area Interior Framing (Wall ó Windows ó Doors)



Pinelands Regional Sr. High School ó Interior Window Frames (Student Locker Room)

### **Epic Management, Inc.** Page 8 of 9





Pinelands Regional Jr. High School ó Boys Restroom (2<sup>nd</sup> floor)



Pinelands Regional Jr. High School ó Boys Restroom (2<sup>nd</sup> floor)

# **Epic Management, Inc.** Page 9 of 9
