



Pinelands Regional School District

Junior & Senior High School Weekly Renovation Updates

Overall Project:

Senior High School - Masonry Restoration

- Continued installation of exterior masonry ó Main Entrance Area, D-Wing block (west) wall
- Continued installation of exterior wall preparation ó steel (installation/cleaning/painting), masonry surface preparation and installation of vapor barrier system
- Continued roof coping modifications
- Continue site clean-up restoration & clean-up ó Gym Area

Senior & Junior High School - Renovations

- Continued selective interior renovations ó (Sr. High School)
- Continued bathroom renovations ó plumbing rough-in, wall framing, ceramic tile, plumbing fixtures (Sr. High School)
- Continued HVAC & Electrical system renovations (Sr. High School)
- Continued bathroom renovation ó 2nd shift work öceramic tileö (1st and 2nd Floor) (Jr. High School)
- Continued layout & installation of Main Entrance Addition öfoundationsö (Sr. High School)
- Continued installation of Gym HVAC unit roof (Sr. High School)
- Continued painting of selective Gym / Bathrooms / Corridor (Sr. High School)
- Continued installation of ceiling system ó Gym Corridor (Sr. High School)
- Commenced installation of doors & hardware ó Gym & Corridor (Sr. High School)
- Commenced general / final clean-up of Gym Phase) Sr. High School)
- Completed installation floor tile & wall base for Gym Corridor (Sr. High School)

Scheduled Activities for the week of December 24 2018 thru December 28 2018

Overall Project:

Senior High School - Masonry Restoration

- Continued layout / modification for new exterior window / door opening
- Continue installation of exterior wall preparation ó steel (installation/cleaning/painting), masonry surface preparation
- Continue installation of exterior masonry ó Entrance Area & D Wing
- Continue roof coping modifications
- Continue site clean-up restoration & clean-up ó Gym Area

Senior & Junior High School - Renovations

- Continue layout & installation of HVAC ductwork (Sr. High School)
- Continue plumbing rough-in / framing / finishes for bathroom renovations (Sr. High School)
- Continue layout / installation for new Main Entrance & Exterior Canopy (Sr. High School)
- Continue Electrical system modifications (Sr. High School)
- Continue installation of Gym HVAC Units (Sr. High School)
- Continue interior selective painting for Gym / Corridor (Sr. High School)
- Continue installation of ceiling system ó Gym Corridor / Bathrooms (Sr. High School)
- Continue general / final clean-up of Gym Phase) Sr. High School)
- Continue selective bathroom renovations ó 2nd shift work (Jr. High School)



Pinelands Regional Sr. High School ó New Gym Entrance & Canopy



Pinelands Regional Sr. High School ó Exterior Masonry Installation (D-Wing West)



Pinelands Regional Sr. High School 6 Exterior Masonry Waterproofing (D-Wing North)



Pinelands Regional Sr. High School 6 Exterior Masonry Waterproofing (D-Wing North)



Pinelands Regional Sr. High School 6 Exterior Masonry Preparation (D-Wing East)



Pinelands Regional Sr. High School 6 Exterior Masonry Preparation (A-Wing West)



Pinelands Regional Sr. High School 6 Exterior Wall Preparation (D Wing South)



Pinelands Regional Sr. High School 6 Structural Steel Installation (D Wing North)




Pinelands Regional Sr. High School 6 Exterior Wall Preparation (Auditorium South)



Pinelands Regional Sr. High School 6 New Main Entrance Addition



Pinelands Regional Sr. High School 6 3rd Floor HVAC Ductwork Installation

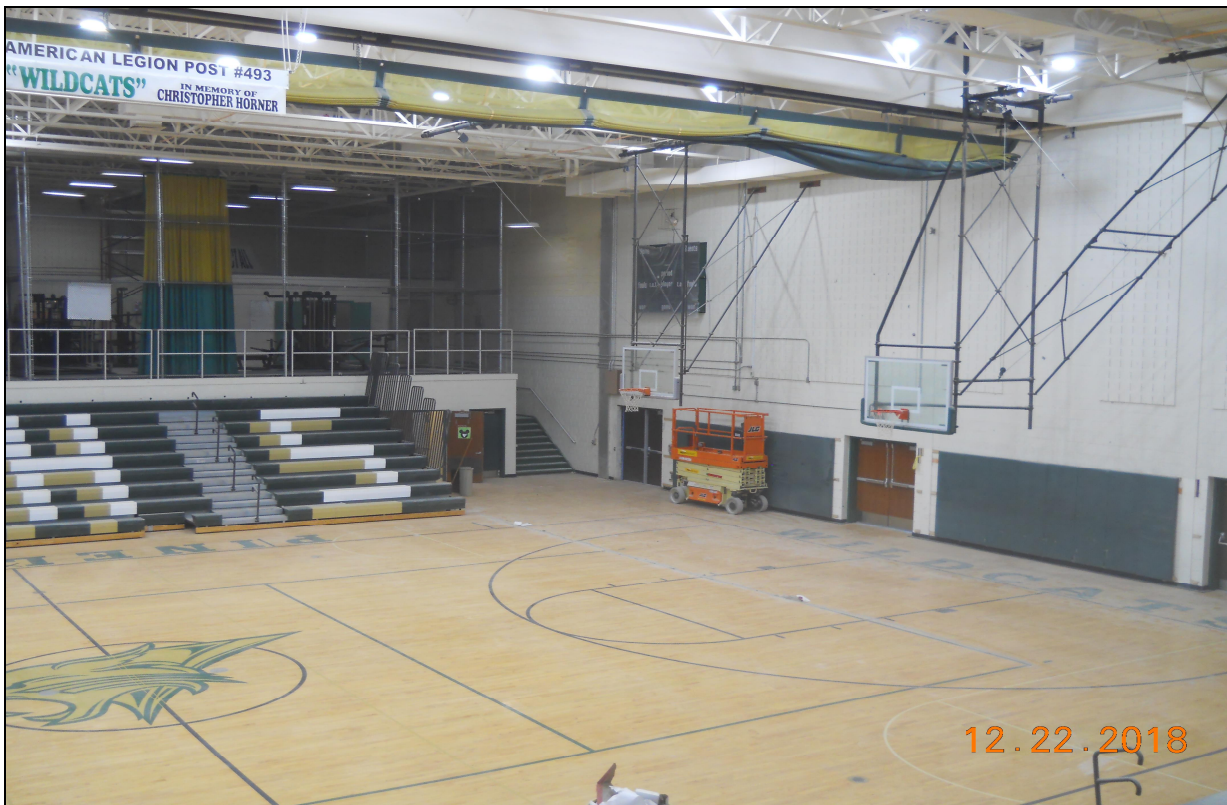

Pinelands Regional Sr. High School 6 Gym Interior



Pinelands Regional Sr. High School 6 Gym Interior



Pinelands Regional Sr. High School Gym Corridor



Pinelands Regional Sr. High School 6 Student Bathroom (Gym Corridor)



Pinelands Regional Jr. High School 6 1st Floor Student Bathroom
