



Pinelands Regional School District

Junior & Senior High School Weekly Renovation Updates

Overall Project:

Senior High School - Masonry Restoration

- Continued installation of Temporary exterior walls
- Continued installation of exterior masonry Gym Area, D-Wing block (east) wall
- Continued installation of exterior wall preparation steel (installation/cleaning/painting), masonry surface preparation and installation of vapor barrier system
- Continued demolition of exterior wall fascia - A-Wing
- Continued roof coping modifications

Senior & Junior High School - Renovations

- Continued selective interior renovations (Sr. High School)
- Continued bathroom renovations plumbing rough-in, wall framing (Sr. High School)
- Continued HVAC & Electrical system renovations (Sr. High School)
- Continued bathroom renovation 2nd shift work (1st and 2nd Floor) (Jr. High School)
- Continued layout & installation of Gym Entrance (Sr. High School)
- Completed installation of Gym HVAC unit roof curbs (Sr. High School)

Senior High School - Athletic Field Renovations

- Continued misc. fencing installation (Athletic Field)

Scheduled Activities for the week of December 03 2018 thru December 07 2018

Overall Project:

Senior High School - Masonry Restoration

- Continue removal of exterior brick fascia, windows and doors (A-Wing)
- Continued layout / modification for new exterior window / door opening
- Continue installation of exterior wall preparation steel (installation/cleaning/painting), masonry surface preparation
- Continue installation of Temporary exterior walls
- Continue installation of exterior masonry Gym Area & D Wing
- Continue roof coping modifications

Senior & Junior High School - Renovations

- Continue layout & installation of HVAC ductwork (Sr. High School)
- Continue plumbing rough-in / framing / finishes for bathroom renovations (Sr. High School)
- Continue layout for new Main Entrance & Exterior Canopy (Sr. High School)
- Continue Electrical system modifications (Sr. High School)
- Continue selective bathroom renovations 2nd shift work (Jr. High School)
- Continue layout / installation of Gym HVAC Units (Sr. High School)
- Commence interior painting of ceiling decking & ductwork Gym (Sr. High School)

Senior High School - Athletic Field Renovations

- Athletic Field Continue misc. site concrete, and asphalt walkway



Pinelands Regional Sr. High School □ Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School □ Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School □ Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School □ Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School □ Exterior Masonry Facia Demolition (A-Wing)



Pinelands Regional Sr. High School □ Exterior Masonry Facia Demolition (A-Wing)



Pinelands Regional Sr. High School □ Exterior Masonry Installation (D-Wing East)



Pinelands Regional Sr. High School □ Exterior Masonry / Steel Installation (D-Wing East)



Pinelands Regional Sr. High School □ Exterior Masonry / Steel Installation (D-Wing East)



Pinelands Regional Sr. High School □ Locker Room (Ceiling Painting / Ductwork)




Pinelands Regional Sr. High School □Locker Room (Ceiling Painting / Ductwork)



Pinelands Regional Sr. High School Gym Roof □New HVAC Unit Curbs



Pinelands Regional Jr. High School- 1st Floor Bathroom Renovations (Student)

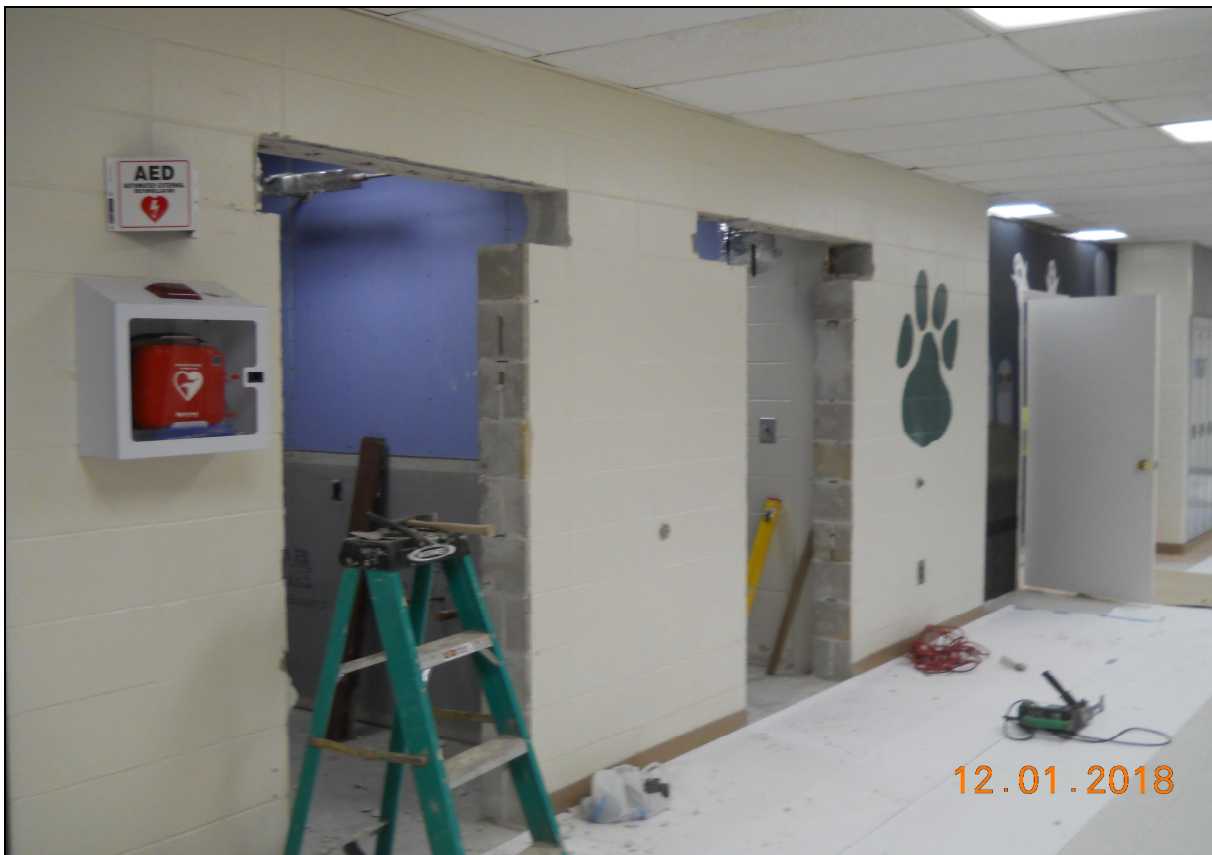

Pinelands Regional Jr. High School □ 2nd Floor Bathroom Renovations (Faculty)
