



Pinelands Regional School District

Junior & Senior High School - Weekly Renovation Updates

Overall Project:

Senior High School - Masonry Restoration

- Continued installation of exterior masonry ó A-Wing elevations
- Continued installation of exterior wall preparation of steel (installation/cleaning/painting), masonry surface preparation and installation of vapor barrier system
- Continued roof coping modifications
- Continued interior wall finishes ó A Wing (north elev.)
- Continued installation of exterior windows & doorsó A Wing North

Senior & Junior High School - Renovations

- Continued selective interior renovations ó (Sr. High School)
- Continued HVAC & electrical system renovations (Sr. High School)
- Completed new Main Entrance addition ó Terrazzo Flooring (Sr. High School)
- Continued preparation & painting for Hallways & Classrooms (Sr. High School)
- Continued installation of ceiling system grid ó selective classrooms & corridors (Sr. High School)
- Commenced interior demolition ó HVAC system, Ceiling systems and selective Bathrooms) Jr. High School)

Senior & Junior High School - Paving & Site Improvements (Spring / Summer 2019)

Continued installation of storm water system (Sr. High)

Scheduled Activities for the week of June 17 2019 thru June 21 2019

Overall Project:

Senior High School - Masonry Restoration

- Continue installation of exterior wall preparation ó steel (installation/cleaning/painting), masonry surface preparation
- Continue installation of exterior masonry \(\delta \) A Wing elevations
- Continue roof coping modifications
- Continue interior wall finishes ó A Wing (north elev.)
- Continue installation of interior window sills & trim (A Wing)
- Continue site concrete work (Sidewalks & Exterior door aprons) & Continue Site/Lawn restoration (A & C Wing)


Senior & Junior High School - Renovations

- Continue layout &installation of HVAC ductwork & units (Sr. High School)
- Continue layout / installation for new Main Entrance 6 Underground Electrical & Drainage (Sr. High School)
- Continue electrical system modifications (Sr. High School)
- Continue preparation & painting of interior walls (Sr. High School)
- Continue ceiling grid & tile installation ó selective classrooms & corridors (Sr. High School)
- Continue installation of VCT floor tile (Corridors & Classrooms) (Sr. High School)
- Continue electrical renovations & fire alarm wiring installation- (Jr. High School)
- Continue renovation mobilization & selective interior demolition (Jr. High School)
- Commence exterior main entrance area demolition (security vestibule & Entrance Canopy) (Jr. High School)
- Commence layout & installation of new HVAC units & ductwork (Jr. High School)
- Commence locker-room renovations ó demolition (Jr. High School)

Senior & Junior High School - Paving & Site Improvements (Spring / Summer 2019)

- Continue installation storm water system installation (Sr. High School)
- Commence Asphalt Paving removal (Sr. High & Jr. High School)

Epic Management, Inc. Page 1 of 9





Pinelands Regional Sr. High School ó Main Entrance õWild Catsö Terrazzo Flooring




Pinelands Regional Sr. High School ó Main Entrance Security Vestibule

Epic Management, Inc. Page 2 of 9





Pinelands Regional Sr. High School ó Exterior Masonry Installation (Block A North)

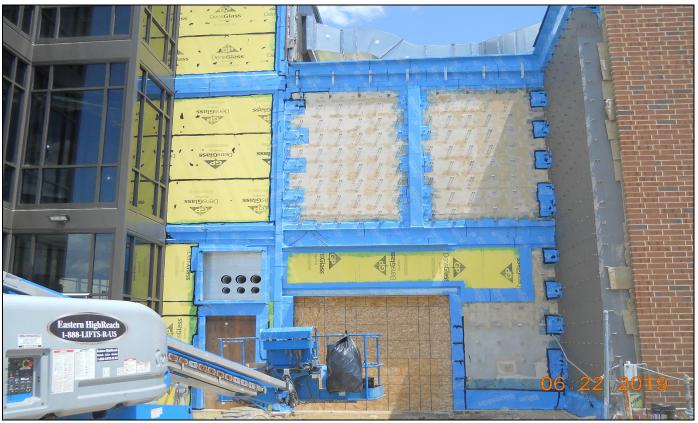

Pinelands Regional Sr. High School ó Exterior Masonry Preparation (Block A West ó Boiler Room)

Epic Management, Inc. Page 3 of 9





Pinelands Regional Sr. High School ó Exterior Facia Preparation / Insulation (Block A South)



Pinelands Regional Sr. High School ó Main Office Carpet Installation

Epic Management, Inc. Page 4 of 9





Pinelands Regional Sr. High School ó Main Office Carpet Installation



Pinelands Regional Sr. High School ó Classroom Interior (Block A North 3rd Floor)

Epic Management, Inc. Page 5 of 9





Pinelands Regional Sr. High School ó Atrium Exterior Elevation (Block A West)



Pinelands Regional Sr. High School ó Media Center Ceiling Light Fixtures

Epic Management, Inc. Page 6 of 9





Pinelands Regional Jr. High School ó Corridor Ceiling System Demolition & Removal (2nd Floor)



Pinelands Regional Jr. High School ó Demolition / Removal of Classroom HVAC Unit (Block C)

Epic Management, Inc. Page 7 of 9





Pinelands Regional Jr. High School ó Classroom Bathroom Demolition



Pinelands Regional Jr. High School ó Heating Plant Equipment Demolition & Removal

Epic Management, Inc. Page 8 of 9





Pinelands Regional Sr. High School ó Storm-water Management System



Pinelands Regional Sr. High School ó Storm-water Management System

Epic Management, Inc. Page 9 of 9
