



Pinelands Regional School District

Junior & Senior High School Weekly Renovation Updates

Overall Project:

Senior High School - Masonry Restoration

- Continued layout / modification for new exterior window / door opening
- Continued installation of ☐Temporary☐exterior walls
- Continued installation of exterior masonry

 Gym Area, D-Wing block (east) wall
- Continued installation of exterior wall preparation □steel (installation/cleaning/painting), masonry surface preparation and installation of vapor barrier system
- Continued demolition of exterior wall facia , Auditorium, A-Wing
- Commenced roof coping modifications

Senior & Junior High School - Renovations

- Continued selective interior renovations

 (Sr. High School)
- Continued bathroom renovations

 plumbing rough-in, wall framing (Sr. High School)
- Continued HVAC & Electrical system renovations (Sr. High School)
- Continued bathroom renovation $\Box 2^{nd}$ shift work (1st and 2nd Floor) (Jr. High School)
- Commenced layout & installation of Gym Entrance column footings (Sr. High School)

Senior High School - Athletic Field Renovations

Continued installation Running Track Surface (Athletic Field)

Scheduled Activities for the week of November 12 2018 thru November 16 2018

Overall Project:

Senior High School - Masonry Restoration

- Continue removal of exterior brick fascia, windows and doors (A-Wing)
- Continued layout / modification for new exterior window / door opening
- Continue installation of exterior wall preparation \(\subseteq \text{steel (installation/cleaning/painting), masonry surface preparation
- Continue installation of Temporary exterior walls
- Continue installation of exterior masonry □Gym Area & D Wing
- Continue roof coping modifications

Senior & Junior High School - Renovations

- Continue layout &installation of HVAC ductwork (Sr. High School)
- Continue plumbing rough-in for bathroom renovations (Sr. High School)
- Continue layout & excavation for new Main Entrance & Exterior Canopy (Sr. High School)
- Continue Electrical system modifications (Sr. High School)
- Continue selective bathroom renovations $\Box 2^{nd}$ shift work (Jr. High School)
- Continue layout / installation of roof curbing for Gym HVAC Units (Sr. High School)

Senior High School - Athletic Field Renovations

- Athletic Field Continue site concrete, fencing installation and asphalt walkway
- Athletic Field □Continue Scoreboard installation
- Athletic Field □Continue installation of Track Surface / Lines

Epic Management, Inc.





Pinelands Regional Sr. High School

Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School

Exterior Masonry Waterproofing / Brick Veneer Installation

Epic Management, Inc. Page 2 of 10





Pinelands Regional Sr. High School

Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School

Exterior Masonry Waterproofing / Brick Veneer Installation

Epic Management, Inc. Page 3 of 10





Pinelands Regional Sr. High School

Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School

Exterior Masonry Waterproofing / Brick Veneer Installation

Epic Management, Inc. Page 4 of 10





Pinelands Regional Sr. High School

Exterior Masonry Wall Installation D-Wing East



Pinelands Regional Sr. High School

Exterior Masonry Facia Demolition Auditorium

Epic Management, Inc. Page 5 of 10

11/10/2018



Pinelands Regional Sr. High School

Exterior Masonry Facia Demolition Auditorium



Pinelands Regional Sr. High School

Exterior Masonry Facia Demolition A-Wing West


Epic Management, Inc. Page 6 of 10





Pinelands Regional Sr. High School

Exterior Masonry Facia Demolition A-Wing West

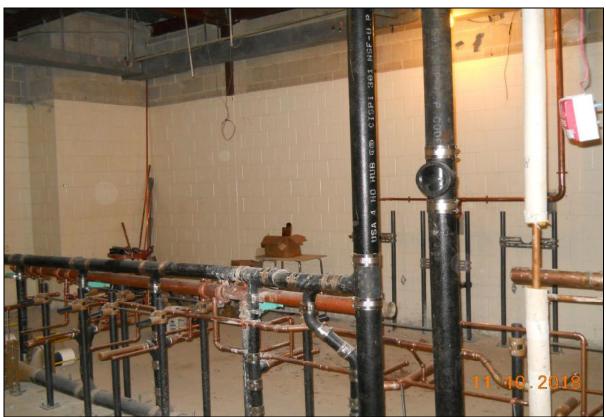

Pinelands Regional Sr. High School □2nd Floor Bathroom Renovations

Epic Management, Inc. Page 7 of 10





Pinelands Regional Sr, High School □1st Floor Bathroom Renovations



Pinelands Regional Sr. High School □1st Floor Corridor / Girls Locker Room Modifications

Epic Management, Inc. Page 8 of 10





Pinelands Regional Sr. High School

Girls Locker Room Ductwork



Pinelands Regional Athletic Field □Track Surfacing

Epic Management, Inc. Page 9 of 10





Pinelands Regional Athletic Field

Track Surfacing



Pinelands Regional Athletic Field □Track Surfacing

Epic Management, Inc. Page 10 of 10
