



Pinelands Regional School District

Junior & Senior High School Weekly Renovation Updates

Overall Project:

Senior High School - Masonry Restoration

- Continued layout / modification for new exterior window / door opening
- Continued installation of -Temporaryö exterior walls
- Continued installation of exterior masonry ó Gym Area; commenced layout for D-Wing block (east) wall installation
- Continued installation of exterior wall preparation of steel (installation/cleaning/painting), masonry surface preparation and installation of vapor barrier system
- Continued demolition of exterior wall facia D-Wing, Auditorium, A-Wing

Senior & Junior High School - Renovations

- Continued selective interior renovations ó (Sr. High School)
- Continued bathroom renovations ó plumbing rough-in (Sr. High School)
- Continued HVAC & Electrical system renovations (Sr. High School)
- Continued bathroom renovation ó 2nd shift work (1st and 2nd Floor) (Jr. High School)
- Completed concrete floor slab restoration ó bathroom renovations (Jr. & Sr. High Schools)
- Commenced installation of HVAC Unit curbs for Gym

Senior High School - Athletic Field Renovations

- Completed installation of Scoreboard Support Columns (Athletic Field)
- Commence installation Running Track Surface (Athletic Field)

Scheduled Activities for the week of November 05 2018 thru November 09 2018

Overall Project:

Senior High School - Masonry Restoration

- Continue removal of exterior brick fascia, windows and doors (A-Wing)
- Continued layout / modification for new exterior window / door opening
- Continue installation of exterior wall preparation of steel (installation/cleaning/painting), masonry surface preparation
- Continue installation of õTemporaryö exterior walls
- Continue installation of exterior masonry ó Gym Area & D Wing

Senior & Junior High School - Renovations

- Continue layout &installation of HVAC ductwork (Sr. High School)
- Continue plumbing rough-in for bathroom renovations (Sr. High School)
- Continue layout & excavation for new Main Entrance & Exterior Canopy (Sr. High School)
- Continue Electrical system modifications (Sr. High School)
- Continue selective bathroom renovations ó 2nd shift work (Jr. High School)
- Continue layout / installation of roof curbing for Gym HVAC Units

Senior High School - Athletic Field Renovations

- Athletic Field óContinue site concrete, fencing installation and asphalt walkway
- Athletic Field ó Continue Scoreboard installation
- Athletic Field ó Continue installation of Track Surface / Lines

Epic Management, Inc.



Pinelands Regional Sr. High School ó Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School ó Exterior Masonry Waterproofing / Brick Veneer Installation

Epic Management, Inc. Page 2 of 10

11/3/2018



Pinelands Regional Sr. High School ó Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School ó Exterior Masonry Waterproofing / Brick Veneer Installation

Epic Management, Inc. Page 3 of 10





Pinelands Regional Sr. High School ó Exterior Masonry Waterproofing / Brick Veneer Installation



Pinelands Regional Sr. High School ó Exterior Masonry Facia Demolition A-Wing West

Epic Management, Inc. Page 4 of 10





Pinelands Regional Sr. High School ó Exterior Masonry Wall Installation D-Wing East




Pinelands Regional Sr. High School ó Exterior Masonry Wall Layout D-Wing East

Epic Management, Inc. Page 5 of 10





Pinelands Regional Sr. High School ó Exterior Masonry Facia Demolition Auditorium

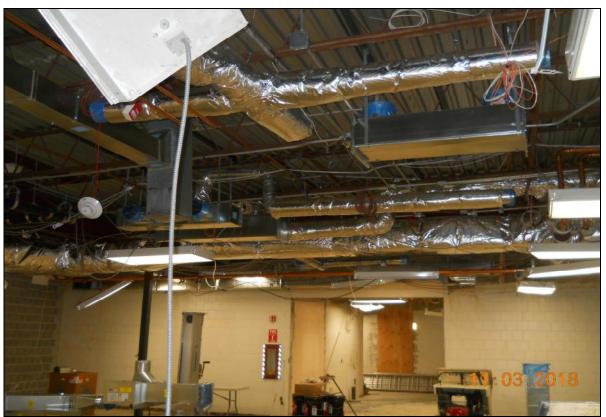

Pinelands Regional Sr. High School ó New HVAC Ductwork Main Office

Epic Management, Inc. Page 6 of 10







Pinelands Regional Sr. High School ó Concrete Floor Restoration Prep

Epic Management, Inc. Page 7 of 10




Pinelands Regional Sr, High School ó Main Office Bathroom Concrete Floor Restoration



Pinelands Regional Jr. High School ó 1st Floor Boys / Girls Bathroom Concrete Floor Restoration

Epic Management, Inc. Page 8 of 10

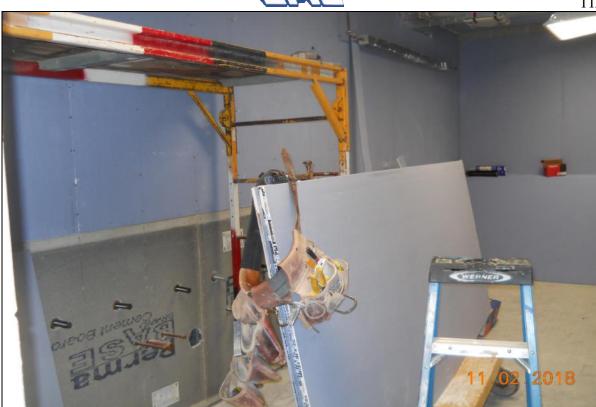

Pinelands Regional Jr. High School ó 2nd Floor Boys / Girls Bathroom Sheetrock wall



Pinelands Regional Jr. High School ó 2nd Floor Boys / Girls Bathroom Wall Framing

Epic Management, Inc. Page 9 of 10





Pinelands Regional Athletic Field ó Scoreboard Support Columns



Pinelands Regional Athletic Field ó Track Base Coat Surface

Epic Management, Inc. Page 10 of 10
